

# PROJECT PLANNING PHASE

## Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

|               |                                                    |
|---------------|----------------------------------------------------|
| Date          | 02 October 2026                                    |
| Project Name  | Automated Network Request Management in ServiceNow |
| Maximum Marks | 5 Marks                                            |

### Product Backlog, Sprint Schedule, and Estimation

| Sprint   | Functional Requirement (Epic)        | User Story Number | User Story / Task                                                         | Story Points | Priority |
|----------|--------------------------------------|-------------------|---------------------------------------------------------------------------|--------------|----------|
| Sprint-1 | Catalog & Form Setup                 | USN-1             | Create Network Request Catalog Item                                       | 3            | High     |
| Sprint-1 | Catalog & Form Setup                 | USN-2             | Configure requester and network request catalog variables                 | 3            | High     |
| Sprint-1 | Catalog & Form Setup                 | USN-3             | Configure Requester Information variable set and Catalog UI Policy        | 3            | High     |
| Sprint-2 | Workflow, Approval & Data            | USN-4             | Configure Flow Designer to retrieve Network Request catalog variables     | 5            | High     |
| Sprint-2 | Workflow, Approval & Data            | USN-5             | Create and map Database Tables (u_database_tables) operational record     | 5            | High     |
| Sprint-2 | Workflow, Approval & Data            | USN-6             | Configure approval action and approval-status branching                   | 3            | High     |
| Sprint-2 | Workflow, Approval & Data            | USN-7             | Maintain REQ/RITM lifecycle and request status context                    | 2            | Medium   |
| Sprint-3 | Notifications, Security & Fulfilment | USN-8             | Configure request-created and request-resolved notifications              | 3            | High     |
| Sprint-3 | Notifications, Security & Fulfilment | USN-9             | Configure Create, Read, Write and Delete ACL access                       | 3            | High     |
| Sprint-3 | Notifications, Security & Fulfilment | USN-10            | Configure Approval Request relationship and operational-record visibility | 3            | High     |
| Sprint-3 | Notifications, Security & Fulfilment | USN-11            | Validate fulfilment handoff and request lifecycle stages                  | 4            | High     |
| Sprint-4 | Testing, Debugging & Deployment      | USN-12            | Test catalog variable retrieval and variable-to-field mappings            | 3            | High     |
| Sprint-4 | Testing, Debugging & Deployment      | USN-13            | Use Flow Execution Details to debug workflow and condition failures       | 2            | Medium   |
| Sprint-4 | Testing, Debugging & Deployment      | USN-14            | Perform end-to-end approval, notification and status testing              | 3            | High     |
| Sprint-4 | Testing, Debugging & Deployment      | USN-15            | Perform UAT and role/security testing                                     | 3            | High     |
| Sprint-4 | Testing, Debugging & Deployment      | USN-16            | Prepare deployment / recreation documentation for a new PDI               | 5            | High     |

### Project Tracker, Velocity & Burndown Chart

| Sprint   | Total Story Points | Duration | Sprint Start | Sprint End (Planned) | Story Points Completed | Release Status |
|----------|--------------------|----------|--------------|----------------------|------------------------|----------------|
| Sprint-1 | 9                  | 5 Days   | Day 1        | Day 5                | 9                      | Completed      |
| Sprint-2 | 15                 | 5 Days   | Day 6        | Day 10               | 15                     | Completed      |
| Sprint-3 | 13                 | 5 Days   | Day 11       | Day 15               | 13                     | Completed      |
| Sprint-4 | 16                 | 5 Days   | Day 16       | Day 20               | 16                     | Completed      |

### Velocity

Total completed story points = 53. Number of sprints = 4. Average team velocity = 53 / 4 = 13.25 story points per sprint.

### Burndown Chart

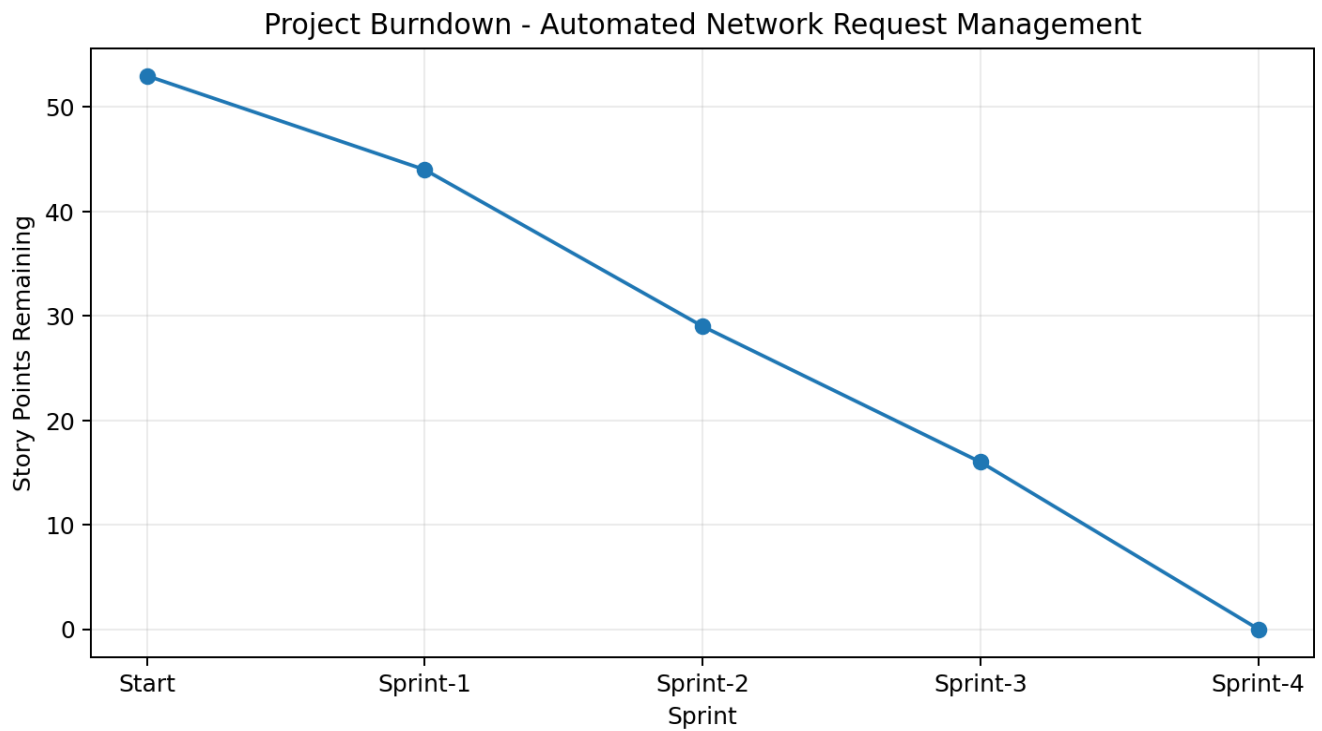


Figure 1. Remaining story points after each completed sprint.

The burndown chart uses the same relative 20-day schedule as the planning template: four 5-day sprints. It represents remaining story points after each sprint and does not claim exact historical calendar dates.

#### Sprint Release Summary

| Sprint   | Release Outcome                                                                                                                                         |
|----------|---------------------------------------------------------------------------------------------------------------------------------------------------------|
| Sprint-1 | Network Request catalog item, requester/network variables, Requester Information variable set, and dynamic form behaviour completed.                    |
| Sprint-2 | Flow Designer automation, catalog-variable retrieval, Database Tables mapping, approval processing, and REQ/RITM request context completed.             |
| Sprint-3 | Request notifications, ACL security, Approval Request relationship, operational visibility, and fulfilment/lifecycle handoff completed.                 |
| Sprint-4 | Variable/mapping tests, Flow Execution debugging, end-to-end workflow testing, UAT/security testing, and deployment/recreation documentation completed. |

**Planning Note:** Exact historical sprint dates and individual team-member assignments were not supplied in the source material. The tracker therefore uses a relative 20-day schedule (four 5-day sprints), while preserving the sprint sequence, backlog structure, story-point estimation, and completed-work format.
